



PIPELINE CROSSING/ENCROACHMENT APPLICATION FORM (WATER / SEWER)

Complete this form and return it along with a non-refundable application fee of \$1,175 (+GST) payable by EFT to "Canadian National Railway Co.". EFT remittance must be emailed to NFCashManagement@cn.ca, and submitted with your application. Credit card payments are NOT accepted.

Regular Applications are a minimum of 6-8 weeks for initial review

Rush Applications are a minimum of 1-2 weeks for initial review

NOTE: Application review times are for applications only, they do not include field reviews, construction or installation of actual crossing. The timeline provided are dependent on workload, work force and material availability therefore they are not guaranteed

DATE:	APPLICANT FILE #:	DRAWING #:
1. Owner / Applicant Information:		
Name: _____		
Address: _____		
Contact Name: _____ Title _____		
Phone Number: _____ Email: _____		
2. Consultant / Land Agent Information:		
Name: _____		
Address: _____		
Contact Name: _____ Title _____		
Phone Number: _____ Email: _____		
3. Location Of Pipeline:		4. Existing Agreement:
CN Mile Post (or nearest Mile Post): _____		If this is a change to an existing crossing, please indicate CN File Number here:
Legal Land Description: _____		
At or Near _____ (Name of City, Town, Village)		5. Please provide a brief description of proposed work (i.e.: OH Wire 65,000 Volts, UG Water Pipeline): _____ _____ _____
GPS Coordinates: Longitude: _____		
Latitude: _____		
6. Pipe Data Checklist:		
<input type="checkbox"/> Inside Diameter of pipe (carrier and casing) <input type="checkbox"/> Outside Diameter of pipe (carrier and casing) <input type="checkbox"/> Wall Thickness of pipe (carrier and casing) <input type="checkbox"/> Pipe Material (carrier and casing) <input type="checkbox"/> Specification /Grade or Class (carrier and casing) <input type="checkbox"/> Yield Strength (min. 241Mpa) (carrier and casing) <input type="checkbox"/> Type of Joint <input type="checkbox"/> Working Pressure <input type="checkbox"/> Cooper E-90 (Design Loading) per TC E-10 <input type="checkbox"/> Max. Operating pressure in pipeline <input type="checkbox"/> Length of Casing Pipe (must extend full width of CN ROW) <input type="checkbox"/> Crossing Angle (must be min. 45 degrees) <input type="checkbox"/> Cathodic Protection Noted (if applicable) <input type="checkbox"/> Hydrostatic pressure carrier pipe tested prior to use <input type="checkbox"/> Burial Depth below track and Right of Way <input type="checkbox"/> Method of Installation <input type="checkbox"/> Commodity		<input type="checkbox"/> Direction of Flow <input type="checkbox"/> Warning Markers <input type="checkbox"/> Shut off Valves <input type="checkbox"/> Plan Number and Date <input type="checkbox"/> Legal Land Description <input type="checkbox"/> Width of CN Right of Way <input type="checkbox"/> Number of Tracks <input type="checkbox"/> Include Note: "Installation and maintenance to be in accordance with TC E10, and the latest edition of applicable CSA Standard Z662" <input type="checkbox"/> Signed and stamped by Professional Engineer <input type="checkbox"/> "For Construction" drawing only (not for construction / preliminary drawings will be declined) <input type="checkbox"/> Completion of GEO-FORM 1, or GEO-FORM 2 if applicable (included) & add appropriate Geotechnical note to your plan if required (5" or greater outside diameter.)



PIPELINE CROSSING/ENCROACHMENT APPLICATION FORM (WATER / SEWER)

7. Geotechnical Information:

Is the pipe outside diameter between 127mm-250mm (5-10 inches): _____

Completed the attached GEO-FORM1: _____

Add following note to your plan: "Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property."

Is the pipe outside diameter greater than 250mm (10 inches): _____

Completed the attached GEO-FORM2: _____

Add following note to your plan: "Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property. Engineer must be on site during construction."

8. Date of Construction:

What is the anticipated start date of this project: _____

*Applications must have this completed form, two (2) copies of an acceptable Engineer designed plan printed on 11 x 17 paper, plus a cover letter, and EFT payment in the amount of **\$1,175.00 plus GST**. Plans must provide sufficient information to determine that installation will meet Railway Standards, General Order requirements and CSA Standards. They must be to scale or have all dimensions shown. They must clearly and accurately show Railway property lines.*

Signature: _____

Date: _____



Applicants must submit one (1) copy of an acceptable plan, cover letter and completed application form. Plans and Installation shall conform to Transport Canada (TC) Standards Respecting Pipeline Crossings under Railways.

The **Non-refundable** Application Fee, in the amount of \$1,175.00 (+GST) to cover the cost of reviewing the applications and plan(s) is due at the time of applications. An additional fee of \$300(+GST) for each review after the initial application due to inadequate or missing information will be charged.

CN GST/HST Registration Number 10076 8779 RT0001, EFT Payable to "Canadian National Railway Co."

Engineering Application Fee* - due with application <input type="checkbox"/> Rush Application Fee	\$1,175.00 (plus GST) <input type="checkbox"/> Add \$3,825.00 (plus GST)
Agreement Fee* (applies to 3m wide x 30m long)	\$2,200.00 (plus GST)
Prepaid Flagging Protection (dependent on location)*	\$950.00 (plus GST)
Prepaid Signals Protection*	\$570.00 (plus GST)
Additional Review Fee*	\$300.00 (plus GST) per review

* The Railway reserves the right to charge for additional costs incurred by the Railway as a result of specific applications. Without limiting the generality, this includes items such as open-cut installations, inductive coordination, charges for train delays and slow orders, consulting and inspection costs. All fees and charges that may be imposed under this Agreement are subject to annual review and adjustment by the Railway.

The Applicant shall indicate the duration of construction on / above / below the CN Right of Way, provide an estimated construction schedule and provide a field contact name and phone number

The following information is require on the drawing:

- Drawings must be to scale or have all dimensions shown
 - A site plan showing the location of crossing in relation to a legal description, road allowance or Railway mileage and subdivision
 - Dimension width of CN Right of Way, the number of tracks and the angle of crossing
 - Direction of flow and location of nearest shut off valves
 - Profile showing the depth of burial from the base of rail and ditch bottom to top of pipe
 - 13.7m clearance to any bridges, building, switches etc.
 - Type of carrier and casing pipes. Wall thickness, and pressures (operating and maximum test). Ensure Cooper E-90 Loading for all designs
 - Pipelines carrying steam, water, sewer and other non-flammable or non-hazardous substances under the Railway shall be encased in STEEL Pipe. Casing pipe may be omitted under the following circumstances:
 - * Under secondary or industrial tracks approved by the CN Engineer, provided maximum operating pressures in the carrier pipe does not exceed 700kPa
 - * For non-pressure sewer crossings where the strength of the pipe and its joints are capable of withstanding railway loading, as approved by the CN Engineer.
 - * For Non-Pressure gravity feed pipe, Coated Corrugated Metal Pipe per AREMA & CSA is acceptable Show the cross-section of the carrier pipe being held clear of the casing pipe by supports / spacers.
- NOTE:** Every Carrier pipe with a diameter of 3 inches or greater shall be held clear of the casing pipe by properly designed supports, insulators or centering devices, installed so that no external loads will be transmitted to the carrier pipe. Grouting of the space between the carrier and casing will NOT be permitted. The ends of the casing pipe shall not be sealed by any load transferring material.
- Warning Markers required on each side of the CN Right of Way
 - Cathodic protection indicated (if applicable)
 - Casing to be extended the full width of the CN Right of Way
 - Method of Installation
 - Contents of Pipe
 - Indicate location of proposed jacking and receiving pits in relation to the gauge side (inside) of nearest rail
 - NOTE: "Installation and maintenance to be in accordance with TC E-10 and the latest edition of applicable CSA Standard Z-662"
 - Professional Engineer Stamp and signature. "Not for Construction" or "Preliminary" drawing are not acceptable.



- Contact Name, Mailing Address, Phone Number, and Email Address
- Revised Drawings must be marked as revised and state reason for revision and date revised
- 11x17 paper size ONLY. Applications received on larger or small paper are classified as inadequate and will be declined

Casing

Carrier Pipe less than 168.3 mm O.D.	Casing Pipe must be a minimum of 50mm O.D larger
Carrier Pipe more than 168.3 mm O.D.	Casing Pipe must be at least 75 mm O.D. larger

- Wall Thickness to be a minimum of 4.8 mm, unless no protective coat or it is not cathodically protected then you must add 1.6 mm (see table 4.10 CSA Z-662 for all sizes)

Minimum Depth of Burial

Below Track	Mainline	Cased	1.68m
Other Tracks		Cased	1.37m
Below Right of Way		Cased	1.00m

Geotechnical Requirements:

- Outside Diameter 5"-10", Completion of GEO-FORM 1 & include note on drawing "Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property".
- Outside Diameter 10" or greater, Completion of GEO-FORM 2 & include note on drawing: "Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property. Engineer must be on site during installation".

Transport Canada Standards Respecting Pipeline Crossings under Railways can be found at:

<https://www.tc.gc.ca/eng/railsafety/standards-tce10-236.htm>

Applications should be emailed to:

<p>NORTHERN ONTARIO, MANITOBA AND SASKATCHEWAN CN Design & Construction Prairie Division Building B, Floor 2 10229-127th Avenue Edmonton, Alberta T5E 0B9</p>	<p>Attention: Sara Lovegrove</p> <p>Phone: (780) 643-7668 Email: praengsvc@cn.ca</p>
<p>ALBERTA AND BRITISH COLUMBIA CN Design & Construction Pacific Division Building B, Floor 2 10229-127th Avenue Edmonton, Alberta T5E 0B9</p>	<p>Attention: Adele Ammar</p> <p>Phone: (780) 472-3041 Email: wcengsvc@cn.ca</p>
<p>BC RAIL TERRITORY CN Design & Construction Pacific Division Building B, Floor 2 10229-127th Avenue Edmonton, Alberta T5E 0B9</p>	<p>Attention: Sara Lovegrove</p> <p>Phone: (780) 643-7668 Email: praengsvc@cn.ca</p>



APPLICATION CHECKLIST – ensure the below required items are sent when applying. Should something be missing, your application will be deemed unacceptable, and you will be required to re-apply accordingly. ***WE DO NOT CONDUCT PRELIMINARY REVIEWS***

Cover Letter

Completed Application Form

Completed GEO-Form 1 / GEO-Form 2 (if pipe has an outside diameter of 5 inches or greater)

1 copy of Signed and Stamped Drawing to Scale – 11 x 17 paper size

EFT payment made payable to “Canadian National Railway Co.” for Application fee plus GST

CONSTRUCTION, OPERATION AND MAINTENANCE OF CROSSINGS

1. The Company shall give the Railway at least ten (10) days' prior notice of its intention to do any construction or maintenance work. The determination of this notice period shall not include Saturdays, Sundays and statutory holidays. Should an emergency situation arise, the Company shall contact the Railway to make special arrangements. The Railway agrees to act reasonably in these situations.
2. Construction and maintenance by the Company of any crossing shall be subject to the supervision of the Railway or the Railway's appointed representatives.
3. Should any work be required to support or repair the tracks or facilities of the Railway or to protect train movements due to the construction, operation, maintenance or removal of crossings, such work shall be performed by the Railway and the Company shall reimburse the Railway for all reasonable costs associated with such work upon receipt of the Railway's account.
4. The Company shall maintain all Crossings under this Agreement in good order and condition in accordance with the applicable rules, requirements and specifications issued from time to time by the Canadian Standards Association and approved by Transport Canada. If at any time during the term of this Agreement, the Company neglects to do any restoration and Maintenance work required to keep any crossing free from hazard, the Railway, after giving reasonable prior written notice to the Company specifying the nature of the work required, may itself carry out such work. The Company shall reimburse the Railway for all reasonable costs associated with this work upon receipt of the Railway's account.
5. The construction, operation and Maintenance of Crossings shall be carried out in a manner so as to minimize interference with Railway Property, facilities and operations. When any such work has been completed, Railway Property shall be restored by the Company to its former condition so far as practicable. The Company shall, at its expense, expeditiously and effectively, remedy any interference that does occur, or, should no appropriate remedy be found, remove such crossing and restore the Railway Property to good order and condition. Should the Company fail to correct such interference, the Railway reserves the right to do so at the Company's expense and the Company will reimburse the Railway upon receipt of the Railway's account therefore.
5. The Railway may impose other construction conditions at time of application.



Geotechnical Requirements

GEO-Form 1

CN Design & Construction

GEO FORM 1

THE APPLICANT MUST COMPLETE THIS FORM, AND SUBMIT WITH UTILITY APPLICATIONS FOR PIPES WITH AN OUTSIDE DIAMETER BETWEEN 5" TO 10".

ONCE COMPLETED, PRINT, AND SIGN THIS FORM.

Note must be added to all plans for pipes between 5 to 10" in outside diameter:

"Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property."

Installations between 5" to 10" in outside diameter:

1. During construction the following must be monitored:
 - a. Ground surface and subsurface movements or settlements
 - Core Main Line
 - i. ANY SETTLEMENTS OF 5MM IS TO BE REPORTED TO CN IMMEDIATELY
 - ii. ANY SETTLEMENTS OF 10MM OR GREATER, WORK IS TO STOP IMMEDIATELY
 - Branch Line
 - i. ANY SETTLEMENTS OF 8MM IS TO BE REPORTED TO CN IMMEDIATELY
 - ii. ANY SETTLEMENTS OF 16MM OR GREATER, WORK IS TO STOP IMMEDIATELY
 - b. Ensure sufficient measures are taken to preserve the safety of rail operations and structural integrity of the track grade.

Please initial here if you understand the above requirements. **Initial** _____

Applicant: _____ Signature: _____

Date Signed: _____ Title: _____



Geotechnical Requirements

GEO-Form 2

CN Design & Construction

GEO FORM 2

THE APPLICANT MUST COMPLETE THIS FORM, AND SUBMIT WITH UTILITY APPLICATIONS FOR PIPES WITH AN OUTSIDE DIAMETER OF 10" OR GREATER.

ONCE COMPLETED, PRINT, AND SIGN THIS FORM.

Note must be added to all plans for installations 10" or greater in outside diameter:

"Geotechnical Engineer evaluation has been completed and the Geotechnical Engineer has determined that based on the soil conditions, there will be no adverse effects to CN operation and property. Engineer must be on site during construction."

Installations 10" or greater in outside diameter:

1. A Geotechnical study must be conducted to ensure there are no known or suspected problems with the installation due to soil conditions at the location. Please provide confirmation that a monitoring and mitigation plan is in place to mitigate potential stability issues with the proposed installation. Review the below requirements and initial indicating compliance and acceptance.
 - a. Construction Methodology relative to soil conditions will be reviewed and identified by the Geotechnical Engineer as a safe and appropriate method of installation.
 - b. Communicate & Rectify potential adverse effects to CN Operations and property.
 - c. The expected extent and magnitude of ground movement over time is expected to be less than the critical threshold in the monitoring plan.
 - d. Set up a contingency plan in the event problems arise during construction at the site and communicate this plan to all parties involved in construction.
 - e. Ground surface and subsurface monitoring in place.
 - f. Vibration limits for communication cables will be considered and will be protected as necessary. If applicable.
 - g. Placed required "note" on application drawing along with stamp and signature.
2. A Geotechnical Engineer must be onsite during installation. Please provide the following:

Firm name: **Name of Geotechnical Firm**
Name of Engineer assigned to project: **Name of Geotechnical Engineer**
Contact number of Engineer assigned to project: **Contact phone number**
Email address of Engineer assigned to project: **Email address of Engineer**




3. During construction Engineer must monitor 24hrs/7days a week:
 - a. Ground surface and subsurface movements or settlements
 - Core Main Line
 - i. ANY SETTLEMENTS OF 5MM IS TO BE REPORTED TO CN IMMEDIATELY
 - ii. ANY SETTLEMENTS OF 10MM OR GREATER, WORK IS TO STOP IMMEDIATELY
 - Branch Line
 - i. ANY SETTLEMENTS OF 8MM IS TO BE REPORTED TO CN IMMEDIATELY
 - ii. ANY SETTLEMENTS OF 16MM OR GREATER, WORK IS TO STOP IMMEDIATELY
 - b. Ensure sufficient measures are taken to preserve the safety of rail operations and structural integrity of the track grade.
4. Post Installation the following is to be done:
 - a. Engineer to provide confirmation in writing that the work was conducted in accordance with the detailed plans accepted by CN. This will include the submission of as-constructed plans with an engineer's stamp.
 - b. Engineer to report on the results of the ground monitoring and confirm that there are no expected problems due to installation

Please initial here as understanding of the above requirements. Initial _____

Applicant: _____ Signature: _____

Date Signed: _____ Title: _____


U/G SEWER & WATER

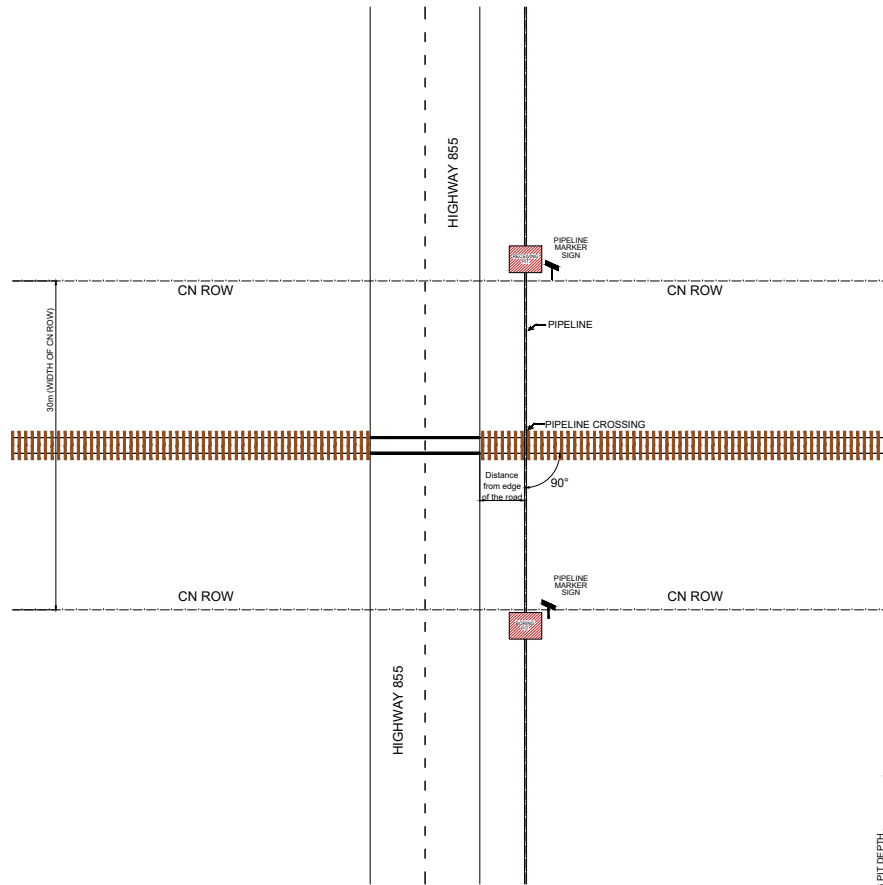

PLAN VIEW
SCALE 1mm : XXm




PROJECT LOCATION
GPS Coordinates: XXX Latitude
XXX Longitude

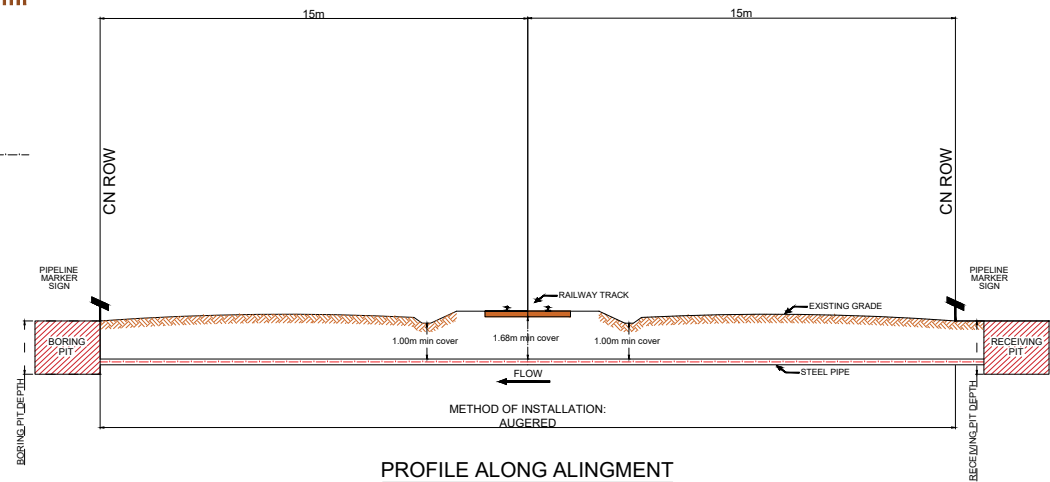

PROFILE ALONG ALIGNMENT
SCALE 1mm : XXm

LEGEND:

EXISTING GRADE
PIPELINE
RIGHT OF WAY
RAILWAY TRACK
EXISTING ROAD



Note:

1. Contractor to arrange CNR S&C locates and flagging prior to construction
2. Boring and Receiving pit should be located outside CN Right of Way
3. Warning Pipeline Marker are to be placed installed outside CN ROW
4. Method of Installation: Boring pit to receiving pit in a manner that the railway grade is not disturbed
5. Installation and maintenance to be in accordance with Transport Canada E-10, and the latest edition of applicable CSA standard Z-662.
7. A Geo-technical Engineer has reviewed the proposed installation work and verified that there are no stability issue with the proposed installation. A Geo-technical Engineer should be on site during construction. (If applicable)

Carrier Pipe Specifications

- a. Contents: xxx
- b. Inside Dia.: x mm
- c. Wall Thickness: x mm
- d. Specifications: xx
- e. Oper./Max. Pres.: xx
- f. Protection: xx
- g. Emergency shutoff valves location: (if not Gravity)

Casing Pipe Specifications

- a. Inside Dia: x mm
- b. Outside Dia: x mm.
- c. Wall Thickness: x mm
- d. Pipe Specifications: x MPa
- e. Length: x m
- f. Material: Steel
- g. Protection: x

REVISIONS

DATE	BY

APPROVALS



OPERATING RAILROAD
XXX SUBDIVISION
XXX MILEAGE
LOCATION

METHOD OF INSTALLATION
FOR
PROPOSED UNDERGROUND UTILITY

OFFICE OF THE PUBLIC WORKS

SHEET X OF X	DRAWN BY: XXX	SCALE: 1mm to XXm	DWG NO:
	CHECKED BY: XXX	DATE: DD MM YY	FILE:

P. ENG. STAMP

DATE
P. ENG. SIGNATURE
